



CONSTRUCTION UPDATE

MONTHLY CONSTRUCTION UPDATE | OCTOBER 2017

Dear Investor,



Lightstone is pleased to update you on the status of Empire State Marriott. The average number of men on-site increased to 180 per day this month.

To date, Lightstone has spent \$93.82 million on construction and acquiring the land. We estimate that over 460 jobs have already been created.


Sincerely,

Jonathan Rabinow
Chief Investment Officer, Lightstone Investments

PROJECT BUDGET

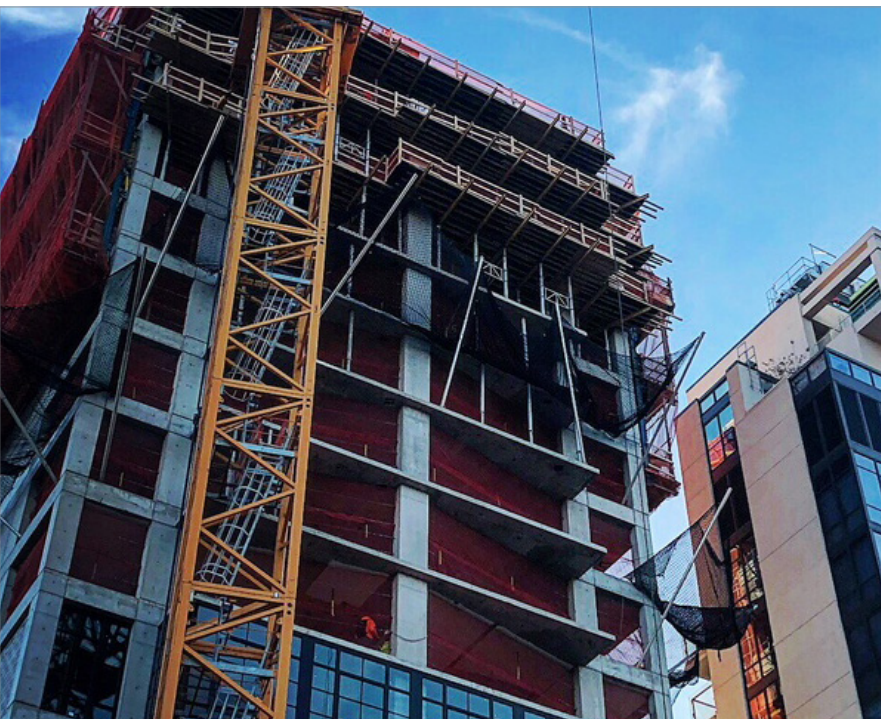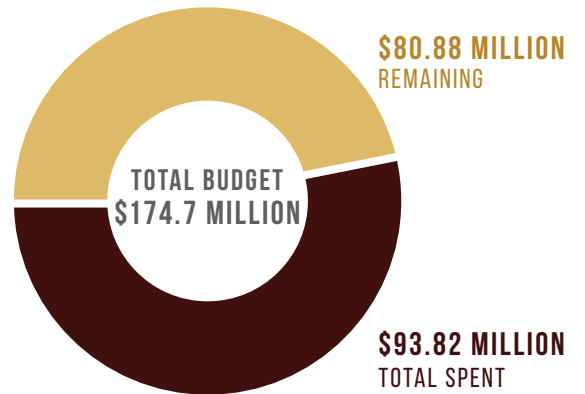

JOB CREATION

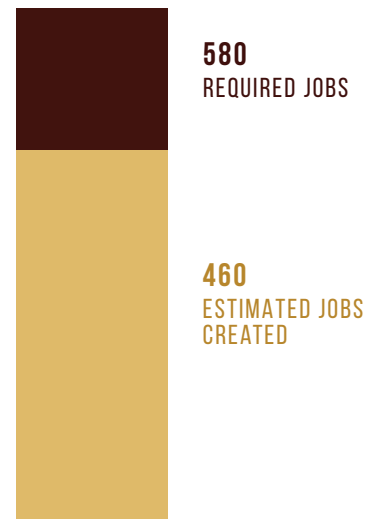

CONSTRUCTION UPDATE

MONTHLY CONSTRUCTION UPDATE | OCTOBER 2017



CONSTRUCTION

MILESTONES

Nearly Completed as of October 2017:

- The concrete superstructure has been built up to the 29th floor. This level of completion allows the construction workers to work on interiors up to that floor.
- Drywall has been installed on the interior from the first floor up to the 9th floor. The drywall makes the interior walls and ceilings.
- The tubing that will contain the heating, ventilation, air conditioning, plumbing, and electrical elements are complete up to the 22nd floor.
- Windows have been installed up to the 23rd floor.
- Metal studs that will soon be covered in drywall for the interior walls and ceilings have been installed up to the 19th floor.
- 90% of the mechanical equipment has been installed on the 3rd floor mechanical room.
- Heat pumps have been installed up to the 20th floors – heat pumps are electrical systems that offer an energy efficient alternative to traditional furnaces and air conditioners.
